# Valley Line West LRT





# **Construction Update**

Status Update – Lane Closures on 104 Avenue between 105 Street and 121 Street AREA 2


This is a supplemental notice for work previously mentioned in the following notice: Lane Closures on 104 Avenue between 105 Street and 121 Street

On April 14, Marigold reduced traffic on 104 Avenue to a single lane in either direction and closed several cross streets, as part of the accelerated roadwork associated with the Valley Line West LRT.

The following is an update on the status of the work scheduled to be completed during the temporary closures.


#### 104 Avenue between 105 Street and 109 Street

- Removal of sidewalks and roadways
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Commencing on or around August 18
- Underground utility work
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Commencing on or around August 18
- Installation of soil cells and tree pits
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Not started
- Installation of permanent streetlights and traffic signals
  - North side of 104 Avenue Below ground work complete, above ground work not started
  - South side of 104 Avenue Not started
- Installation of permanent concrete curbs, sidewalks and pavement
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Not started
- Track slab installation Not started

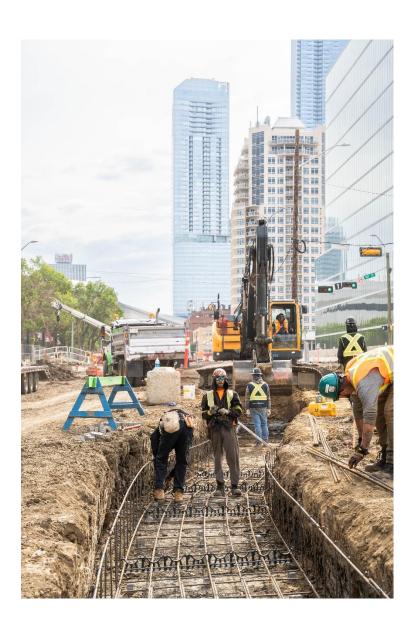


#### 104 Avenue between 109 Street and 116 Street

- Removal of sidewalks and roadways
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Underground utility work
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Installation of soil cells and tree pits
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Not applicable
- Installation of permanent streetlights and traffic signals
  - North side of 104 Avenue Below ground work complete, above ground work not started
  - South side of 104 Avenue Ongoing
- Installation of permanent concrete curbs, sidewalks and pavement
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Track slab installation Ongoing

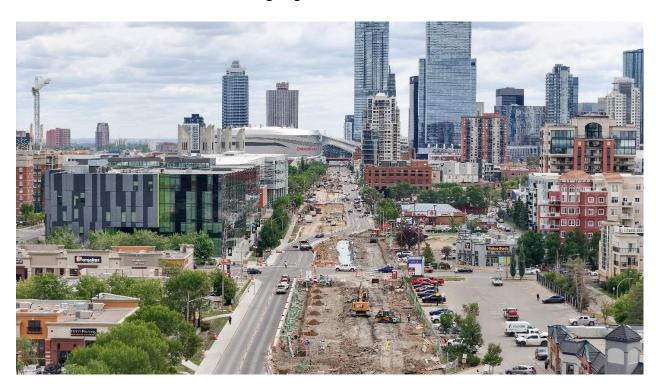

#### 104 Avenue between 116 Street and 121 Street

- Removal of sidewalks and roadways
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Underground utility work
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Installation of soil cells and tree pits
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Installation of permanent streetlights and traffic signals
  - North side of 104 Avenue Below ground work complete, above ground work not started
  - South side of 104 Avenue Ongoing
- Installation of permanent concrete curbs, sidewalks and pavement
  - North side of 104 Avenue Complete
  - South side of 104 Avenue Ongoing
- Track slab installation Ongoing

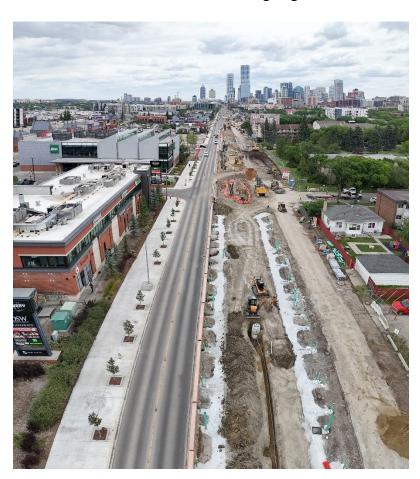

The remaining work is anticipated to last until the end of November.

The information in this bulletin is current to August 14, 2025. Please note that all dates are approximate and weather dependent. We thank you for your patience during construction of the Valley Line West LRT project.

### **Contact Us**

# **Marigold Infrastructure Partners (for construction inquiries)**

Visit: marigoldinfra.ca

Email: <a href="mailto:public@marigoldinfra.ca">public@marigoldinfra.ca</a>

Call: 780-412-2183

Follow us on: 🗗 🕏

## **City of Edmonton (for general project inquiries)**

Visit: edmonton.ca/valleylinewest Email: <a href="mailto:lrtprojects@edmonton.ca">lrtprojects@edmonton.ca</a>

Call: LRT Projects Information Centre at 780-496-4874 (voicemail)
