

Construction Update

Status Update – Partial Closure of Stony Plain Road and 156 Street Intersection AREA 4

This is a supplemental notice for work previously mentioned in the following notice:


[Temporary Partial Closure of Stony Plain Road and 156 Street Intersection](#)

On April 21, Marigold initiated the temporary partial closure of Stony Plain Road at 156 Street intersection, as part of the accelerated roadwork associated with the Valley Line West LRT.

The following is an update on the status of the work scheduled to be completed during Stage One of the temporary partial closure.

- Removal of sidewalks and roadways – *complete for Stage One*
- Underground utility work – *complete for Stage One*
- Installation of soil cells – *complete for Stage One*
- Installation of permanent streetlights & traffic signals – *base and conduit installation complete for Stage One*
- Installation of track slab – *anticipated to start the week of May 12*
- Installation of permanent concrete curbs, sidewalks and pavement and tree pits – *not started (this is one of the final scopes of work scheduled)*

Once Stage One is complete, Marigold will begin Stage Two, which is anticipated to take approximately six weeks.

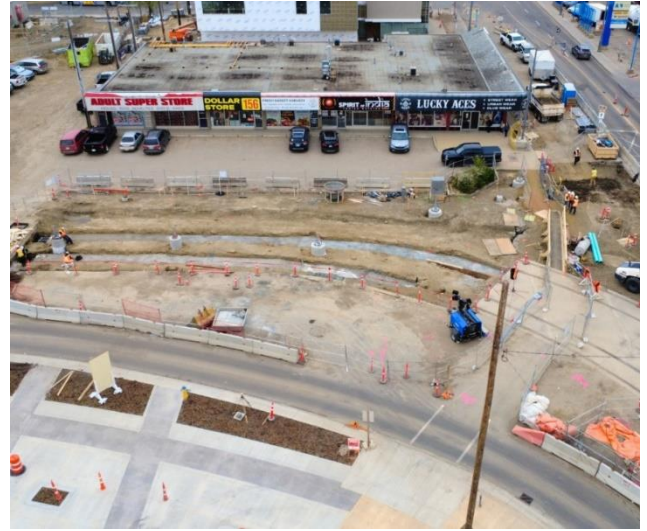

The information in this bulletin is current to May 12, 2025. Please note that all dates are approximate and weather dependent. We thank you for your patience during construction of the Valley Line West LRT project. Marigold Infrastructure Partners is excited to be a part of Edmonton's economic recovery.

Contact Us

Marigold Infrastructure Partners (for construction inquiries)

Visit: marigoldinfra.ca

Email: public@marigoldinfra.ca

Call: 780-412-2183

Follow us on:   

City of Edmonton (for general project inquiries)

Visit: edmonton.ca/valleylinewest

Email: lrtprojects@edmonton.ca

Call: LRT Projects Information Centre at 780-496-4874 (voicemail)
